ID	Task Name	Duration	Start	Finish
1	Bid Period	45 edays	Wed 9/1/10	Sat 10/16/10
2	Award contract	30 edays	Sat 10/16/10	Mon 11/15/10
3	Notice to Proceed	0 days	Mon 11/15/10	Mon 11/15/10
4				
5	**Phase 2 Collection System**	**236 days?**	**Mon 11/15/10**	**Mon 10/10/11**
6	Mobilization	30 edays	Mon 11/15/10	Wed 12/15/10
7	Erosion control 1200 C permit	30 edays	Wed 12/15/10	Fri 1/14/11
8	Submittals	45 days?	Wed 12/15/10	Tue 2/15/11
9	Pipeline <5 ft depth, 36,000 ft	120 days	Tue 3/1/11	Mon 8/15/11
10	Pipeline >5 ft depth, 10,000 ft	50 days	Mon 7/11/11	Fri 9/16/11
11	Pavement replacement	119 days	Tue 4/12/11	Fri 9/23/11
12	Boring I-5, 42-dia, 400 ft	90 edays	Fri 7/1/11	Thu 9/29/11
13	Stubs and boxes for 376 lateral connections	120 days	Tue 4/26/11	Mon 10/10/11
14				
15				
16	**Phase 3 Wastewater Treatment Facility**	**358 days**	**Mon 11/15/10**	**Thu 3/29/12**
17	Mobilization	3 ewks	Mon 11/15/10	Mon 12/6/10
18	Access Road, bridge, power and water	60 edays	Mon 12/6/10	Fri 2/4/11
19	Erosion control 1200C permit	45 edays	Mon 11/15/10	Thu 12/30/10
20	Submittals	90 edays	Mon 12/6/10	Sun 3/6/11
21	Strip topsoil, rock for staging area	30 edays	Mon 4/4/11	Wed 5/4/11
22	Pipelines thru wetlands	60 edays	Thu 9/1/11	Mon 10/31/11
23	Lagoon Construction	90 edays	Fri 7/1/11	Thu 9/29/11
24	Aeratoin basin excavation and concrete	8 emons	Wed 5/4/11	Fri 12/30/11
25	Chlorine contact basin excavation and concrete	6 emons	Wed 5/4/11	Mon 10/31/11
26	Equipment Building	4 emons	Wed 5/4/11	Thu 9/1/11
27	Mechanical equipment installation	6 emons	Thu 9/1/11	Tue 2/28/12
28	Electrical and controls	6 emons	Thu 9/1/11	Tue 2/28/12
29	Testing and startup	30 edays	Tue 2/28/12	Thu 3/29/12
30				
31	**Phase 4 STEP Tanks**	**512 days?**	**Tue 11/30/10**	**Wed 11/14/12**
32	Design	168 days?	Tue 11/30/10	Thu 7/21/11
33	Bidding	80 edays	Thu 7/21/11	Sun 10/9/11
34	Construction	165 days?	Thu 3/29/12	Wed 11/14/12

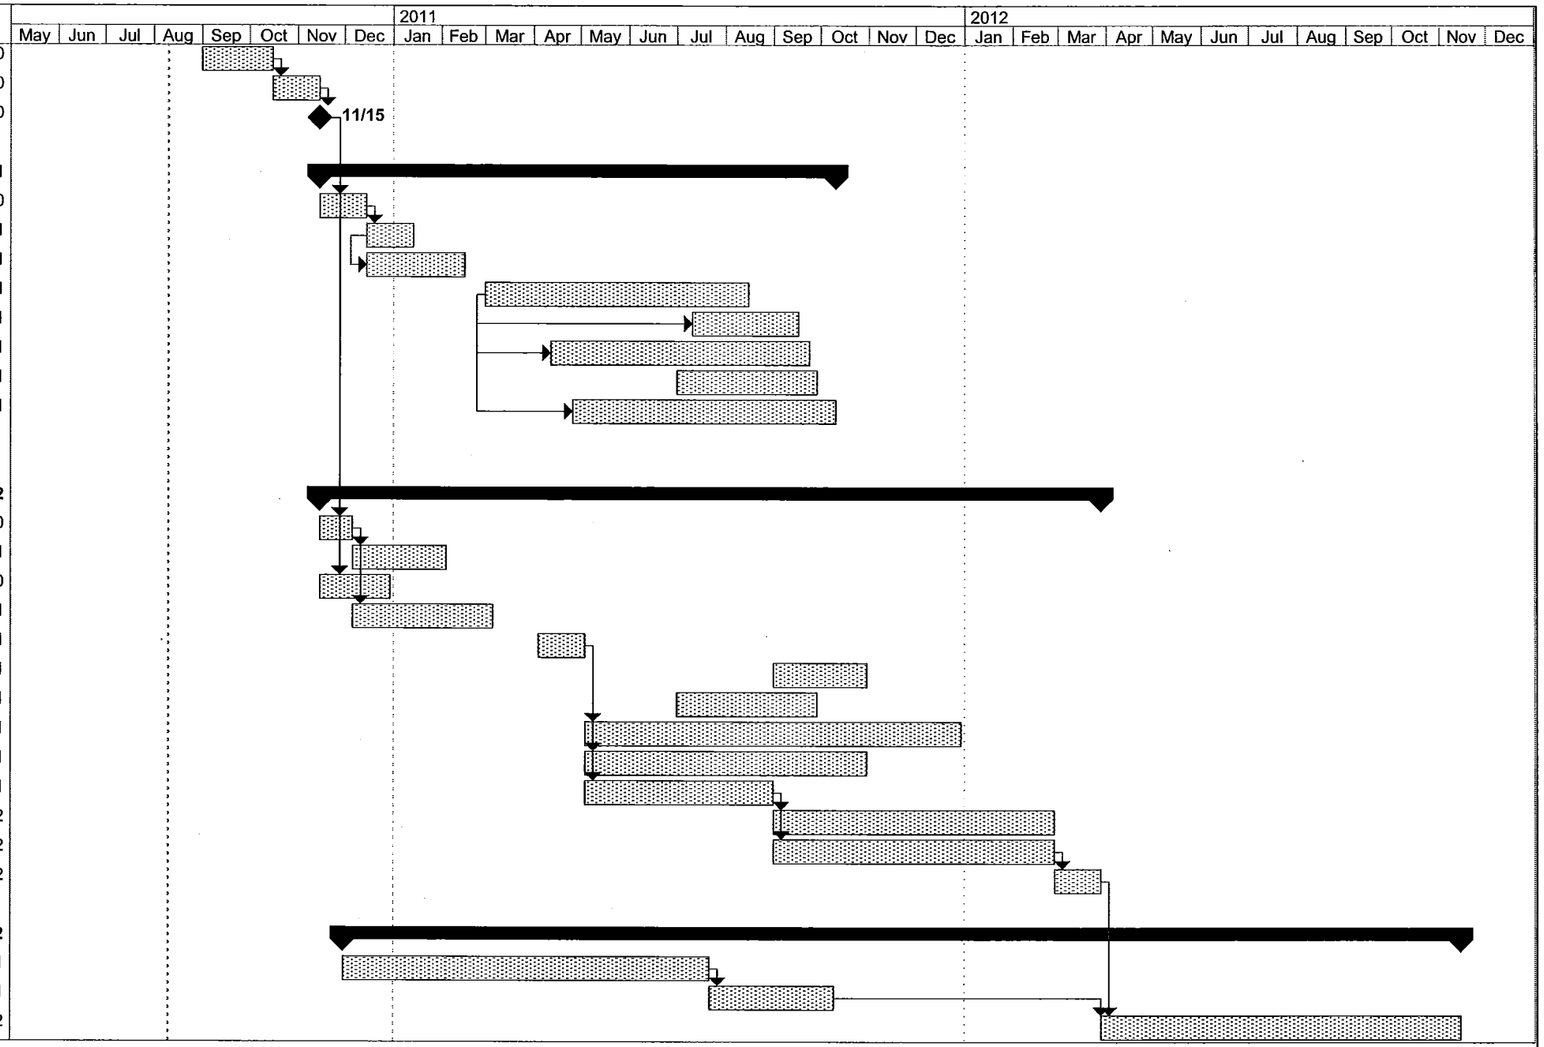

Project: PreConstruction Schedule, re
Date: Tue 8/10/10

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
